

Nika Arts Studio

Project Management Dashboard


Project window: 24 May 2026 to 13 June 2026 | Delivery model: Codex-assisted build, test, deployment, and production support

Executive Dashboard


Current production status and business outcomes

Area	Status	Business outcome
Customer storefront	Done	Browse products, view details, choose colors, build custom bouquets, add to cart, and place manual UPI orders.
Admin operations	Done	Manage products, stock, images, categories, orders, payment verification, dashboard metrics, and site content.
Cloud storage	Done	Product, logo, hero, and artist images moved from local storage to Cloudinary.
Database	Done	SQLite migrated to Supabase Postgres for production data.
Payments	Partial	Manual UPI implemented. PhonePe paused until business account approval.
Shipping	Partial	Shiprocket mock/test support implemented; live use pending final account/pickup verification.
Production hosting	Done	GitHub + Render + custom domain flow established.

Estimated effort by work type

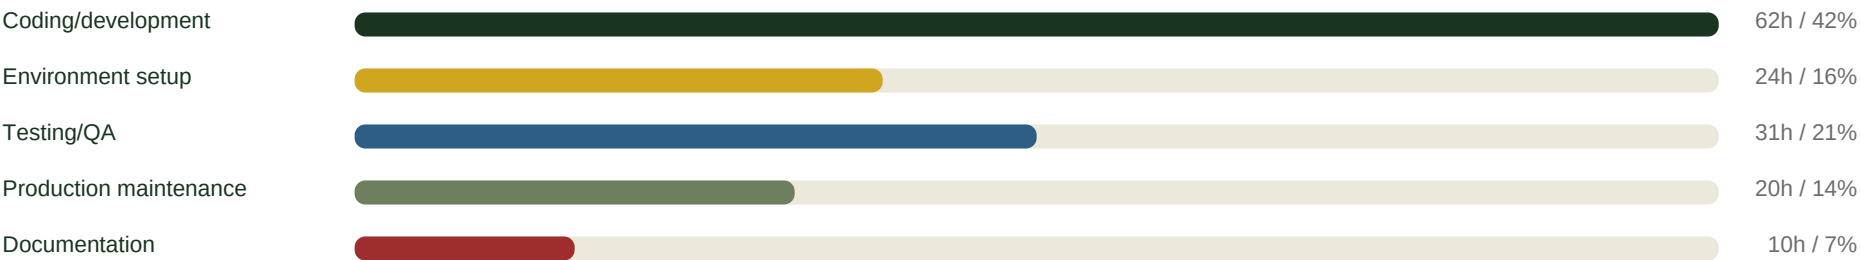


Delivery timeline: 24 May to 13 June 2026

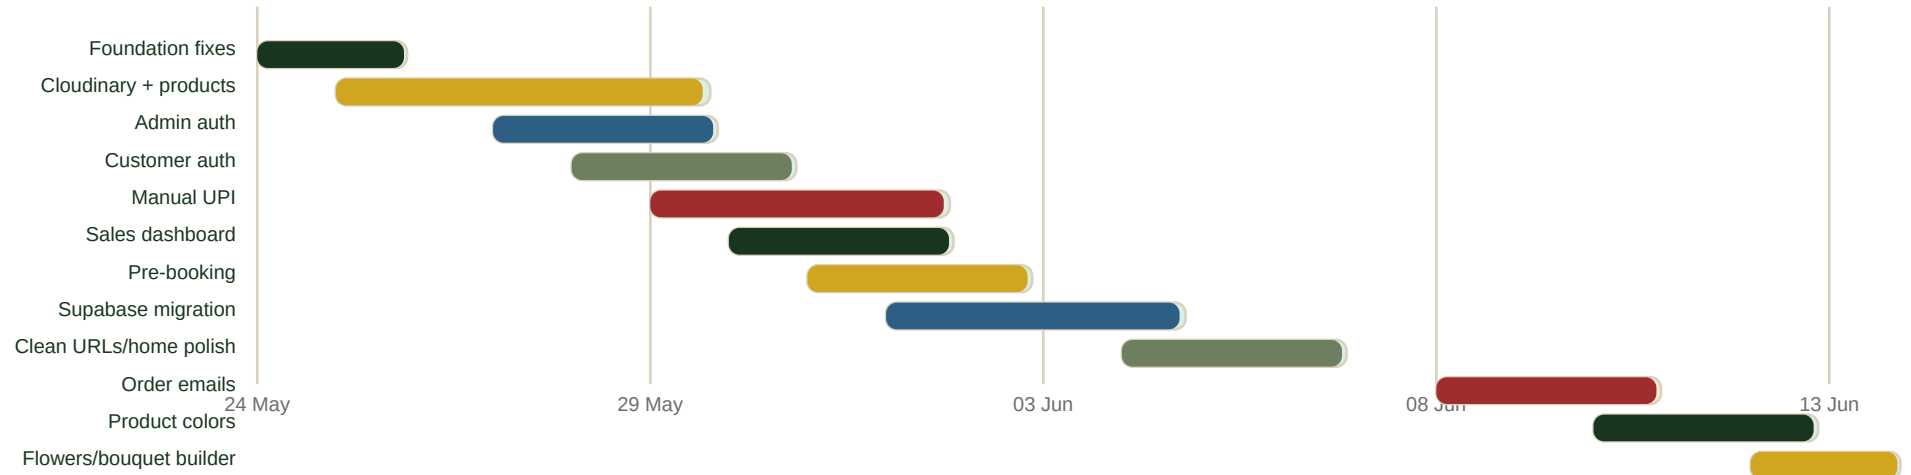

Architecture Snapshot

How customer/admin experiences connect to services

Current production architecture

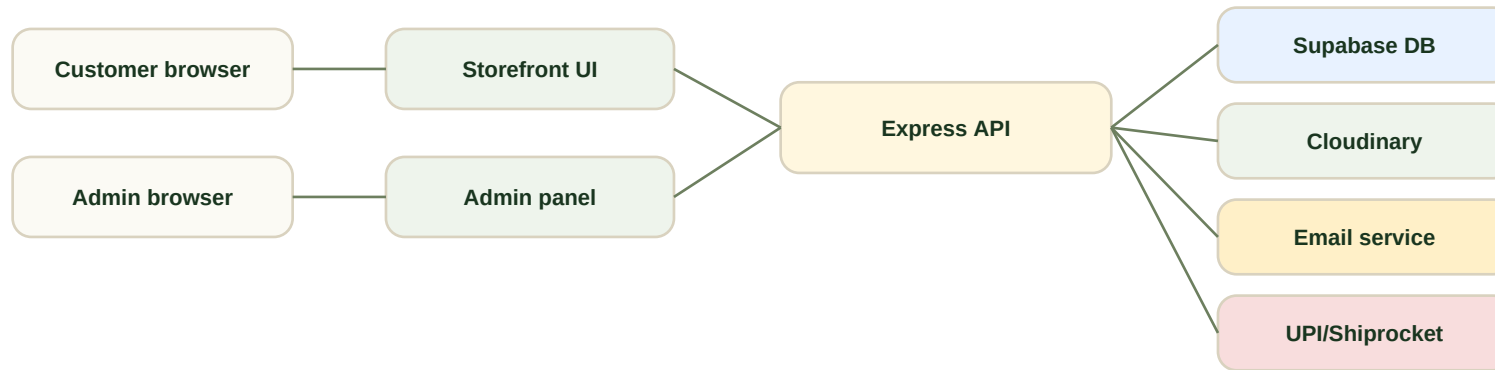

Epic	Objective	Status	Key acceptance criteria
E1. Storefront foundation	Build customer-facing shopping website.	Done	Clean URLs, products from API, mobile-friendly browsing, cart and checkout available.
E2. Cloud image management	Move product and site images to free cloud storage.	Done	Cloudinary uploads work and storefront/admin load cloud URLs.
E3. Admin inventory operations	Give layman admin a clean catalog manager.	Done	Add, edit, hide, delete, search, filter, import/export, and stock update work.
E4. Authentication and security	Secure admin/customer access.	Done	Login/logout/password reset/change work; passwords are hashed.
E5. Supabase migration	Replace local SQLite with hosted Postgres.	Done	Products, customers, orders, sessions, categories, and settings persist in Supabase.
E6. Manual UPI order flow	Enable payments before PhonePe approval.	Done	Customer submits UPI reference; admin confirms payment before paid status.
E7. Order communication	Notify customer/admin by email.	Partial	Templates and confirmation links exist; production provider validation remains.
E8. Shipping/logistics	Prepare Shippo integration.	Partial	Mock mode works; live credentials/pickup final verification pending.
E9. Admin dashboard/reporting	Provide sales visibility.	Done	Overall/product-level sales, recent orders, and all-orders page available.
E10. Pre-booking	Reserve out-of-stock products.	Done	Half-price advance, balance payment after stock restore, then shipping.
E11. Product variants	Support color choices.	Done	Admin color/image setup and customer-selected image switching.
E12. Custom bouquet builder	Let customers compose bouquets.	Done	Separate category, selectable flower sticks, realistic preview, reset, and estimate.
E13. Production operations	Make deployment maintainable.	Done	GitHub/Render/domain/env documentation and branch flow established.

User Story Register

Detailed story breakdown with effort and acceptance criteria

ID	Epic	Story	Pri	Effort	Pts	Status	Acceptance criteria
US-001	E1	Home page introduces Nika Arts Studio and links to shop/about/contact.	P1	Dev + QA	5	Done	Home loads with Cloudinary hero/logo assets and clear navigation.
US-002	E1	Browse all products and filter by category.	P1	Dev	5	Done	Shop loads products from API; category filters work.
US-003	E1	Clean URLs without .html.	P2	Dev + prod	3	Done	/, /shop, /admin, /track-order route correctly.
US-004	E1	Mobile-friendly product cards.	P1	QA + frontend	3	Done	Buttons fit; detail back link returns to selected category.
US-005	E2	Store product images in Cloudinary.	P1	Env + dev	8	Done	Uploads return URLs and images load in admin/storefront.
US-006	E2	Bulk upload Cloudinary products by CSV.	P1	Dev + QA	8	Done	CSV template/import works; duplicate cleanup is possible.
US-007	E2	Load logo/artist images from Cloudinary.	P2	Dev	3	Done	Site assets are configurable and cloud-hosted.
US-008	E3	Compact admin inventory view.	P1	Frontend + QA	5	Done	Search, filters, sorting, aligned action buttons.
US-009	E3	Remove duplicate/old products.	P1	Backend + QA	5	Done	Delete works for manual and CSV products with in-house confirmation.
US-010	E3	Smaller edit stock modal.	P2	Frontend QA	2	Done	Save button reachable without relying on Enter key.
US-011	E4	Secure admin login/logout.	P1	Backend + security	8	Done	Seeded admin, hashed password, server-side sessions.
US-012	E4	Admin password management.	P1	Backend + QA	5	Done	Admin can change password; old password fails.

User Story Register

Continued

ID	Epic	Story	Pri	Effort	Pts	Status	Acceptance criteria
US-013	E4	Customer signup/login/logout.	P1	Backend + UI	8	Done	Customer can register, login, logout, and view account/orders.
US-014	E4	Customer forgot/reset password.	P1	Backend + email	8	Done	Tokenized reset links use BASE_URL.
US-015	E5	Cloud database storage.	P1	Env + backend	13	Done	Supabase pooler works; data persists after deploy.
US-016	E5	Migration tests.	P1	QA	5	Done	Smoke scripts validate products/auth/checkout initiation.
US-017	E6	Manual UPI checkout.	P1	Backend + UI	8	Done	UPI ID/QR/reference captured; pending order created.
US-018	E6	Admin payment verification.	P1	Backend + admin	8	Done	Confirmation screen updates payment/order status.
US-019	E7	Customer order emails.	P1	Email + QA	5	Partial	Template exists; production provider validation remains.
US-020	E7	Admin order notification emails.	P1	Email + admin	5	Partial	Admin email includes order details and confirm link.
US-021	E8	Shiprocket testing without live charges.	P1	Backend + test env	5	Done	Mock serviceability/order/tracking responses available.
US-022	E8	Live Shiprocket fulfillment.	P1	Env + prod	8	Pending	Live serviceability, AWB, and tracking verified.
US-023	E9	Overall sales dashboard.	P1	Dashboard dev	5	Done	Overall sales separated from individual product sales.
US-024	E9	Product-level sales reports.	P1	Backend + UI	5	Done	Dropdown filters metrics to selected product only.

User Story Register

Continued

ID	Epic	Story	Pri	Effort	Pts	Status	Acceptance criteria
US-025	E9	Recent orders and all-orders page.	P2	Full stack	5	Done	Latest 5 on dashboard; full page retains admin actions.
US-026	E10	Pre-book out-of-stock products.	P2	Business logic	8	Done	Half-price advance and pending balance recorded.
US-027	E10	Notify when stock returns.	P2	Email + status	5	Done	Balance flow available after stock restore.
US-028	E11	Admin adds product colors.	P1	Data + admin UI	8	Done	Multi-color flag, color names/images, default behavior.
US-029	E11	Customer image changes by color.	P1	Frontend QA	5	Done	Selected color updates image; refresh returns to default.
US-030	E12	Build custom bouquet.	P2	Frontend + logic	8	Done	Select, visualize, reset, and estimate from product prices.
US-031	E12	Realistic bouquet preview.	P2	Visual QA	5	Done	Reference bouquet image and full-stick overlays used.
US-032	E13	GitHub source of truth.	P1	DevOps	5	Done	Main branch contains production code; Render deploys from GitHub.
US-033	E13	Production env documentation.	P1	Docs	3	Done	Required env vars listed in README.
US-034	E13	Admin/end-user guide.	P2	Docs	5	Done	Guide covers operations, privileges, pending tasks, troubleshooting.

Acceptance Criteria by Epic

Definition of successful delivery

Epic	Acceptance criteria
E1. Storefront Foundation	- Root domain opens the site. - Shop/product/cart/checkout/success/account/track pages work without .html. - Products are API-driven. - Mobile and desktop layouts remain usable.
E2. Cloud Image Management	- Credentials stay in env variables. - Product images upload to Cloudinary. - Logo/hero/artist images load from cloud. - Broken images degrade gracefully.
E3. Admin Inventory Operations	- Admin can create, edit, hide, delete, search, filter, import/export. - Duplicate products can be removed. - Inventory remains usable as catalog grows. - Edit modal fits smaller screens.
E4. Authentication and Security	- Passwords are hashed. - Sessions expire. - Password reset uses tokenized BASE_URL links. - Errors do not leak sensitive details.
E5. Supabase Migration	- Core tables exist in Postgres. - Migration is repeatable and safe. - Render uses Supabase pooler. - Smoke tests prove data is available.
E6. Manual UPI Order Flow	- Guest/logged-in checkout works. - No sensitive UPI PIN/card data collected. - Order stays pending until admin verifies. - Verification updates order/payment status.
E7. Order Communication	- Customer and admin templates include order details. - Admin link can confirm payment. - Provider failures are logged. - Production sender/domain is validated.
E8. Shipping and Logistics	- Test uses mock mode. - Production uses live mode only when configured. - Admin can update fulfillment. - Customer tracking reflects progress.
E9. Admin Dashboard and Reporting	- Overall and product sales are separate. - Dropdown filters product metrics. - Recent orders limited to 5. - All-orders page keeps actions.
E10. Pre-Booking	- Out-of-stock shows pre-book. - Advance is half price. - Balance is payable after restock. - Shipping waits for full payment.
E11. Product Variants	- Admin controls multi-color flag. - Selector appears only for multi-color products. - Image/cart/order respect selected color. - Default color returns on fresh load.

Epic	Acceptance criteria
E12. Custom Bouquet Builder	- Category appears separately. - Selections are highlighted. - Preview/reset can be repeated. - Estimate uses selected flower prices. - Preview looks bouquet-like.
E13. Production Operations	- Changes are pushed through GitHub. - Render env vars are documented. - DNS/domain setup is documented. - Pending integrations are clearly tracked.

Risks, Backlog, and Sprint Mapping

Operational items that still need attention

Risk	Probability	Impact	Mitigation
Email delivery works in test but not production	Medium	High	Validate Resend domain/sender, keep Gmail fallback optional, log provider failures.
Shiprocket live setup incomplete	Medium	High	Keep mock mode in test; validate pickup and serviceability before live mode.
PhonePe business approval delayed	High	Medium	Continue manual UPI until account and website verification are complete.
Supabase/provider account lockout	Medium	High	Maintain recovery codes, backup owner access, and DB export routine.
Render free tier cold starts	High	Medium	Accept early stage; upgrade when volume grows.

Backlog item	Priority	Acceptance criteria
Complete Shiprocket live order creation	P1	Paid order creates shipment, stores AWB/tracking, and updates customer tracking.
Complete production email provider validation	P1	Customer/admin receive real production emails for order placed and payment confirmed.
PhonePe integration after business approval	P2	PhonePe verifies website and callbacks reconcile payment status.
Supabase backup/export process	P1	Weekly manual or automated export is documented and tested.
Admin audit log	P2	Product/order/payment changes show actor, timestamp, old/new values.
Bulk stock editor	P2	Admin updates stock for many products from one screen.

Sprint	Dates	Theme	Main deliverables
Sprint 1	24-28 May	Foundation and cloud migration	Storefront review, Cloudinary image flow, admin inventory, admin auth.
Sprint 2	29 May-02 Jun	Commerce and database hardening	Customer auth, manual UPI, order tracking, sales dashboard, Supabase migration.
Sprint 3	03-08 Jun	Production readiness	GitHub/Render/domain recovery, clean URLs, README/admin guide, email templates.
Sprint 4	09-13 Jun	Catalog growth and advanced UX	Product colors, flower category, custom bouquet builder, mobile/category fixes.

Definition of done: code committed to correct branch, environment documented, UI previewed when visual, happy path and edge cases tested, production impact understood, and docs updated when operational behavior changes.
